



Entergy New Orleans, LLC
1600 Perdido Street 70112-1208
P.O. Box 61000
New Orleans, LA 70161-1000
Tel 504-670-3680
Fax 504-670-3615
cnicho2@entergy.com

Courtney R. Nicholson
Vice-President – Regulatory and Public Affairs

December 15, 2021

Via Electronic Delivery

Ms. Lora W. Johnson, CMC, LMMC
Clerk of Council
City Hall - Room 1E09
1300 Perdido Street
New Orleans, LA 70112

Re: Resolution Directing Entergy New Orleans, Inc. to Investigate and Remediate Electric Service Disruptions and Complaints and to Establish Minimum Electric Reliability Performance Standards and Financial Penalty Mechanisms – CNO Docket No. UD-17-04

Dear Ms. Johnson:

Please find enclosed for your further handling Entergy New Orleans, LLC's ("ENO") 2021 Reliability Plan Project Status Report through September 30, 2021, which is being submitted for filing in the above-referenced docket pursuant to Council Resolution R-18-98. As a result of the remote operations of the Council's office related to COVID-19, ENO submits this filing electronically and will submit the requisite original and number of hard copies once the Council resumes normal operations, or as you direct. ENO requests that you file this submission in accordance with Council regulations as modified for the present circumstances.

Thank you for your assistance with this matter.

Sincerely,

A handwritten signature in blue ink that reads "Courtney R. Nicholson".

Courtney R. Nicholson

CRN\bkd

Enclosures

cc: Official Service List (UD-17-04 via *electronic mail*)

**ENTERGY NEW ORLEANS, LLC'S
RELIABILITY PROJECT STATUS REPORT AS SEPTEMBER 30, 2021**

Entergy New Orleans, LLC (“ENO”) respectfully submits this Reliability Project Status Report to provide the Council with an update through September 30, 2021 on progress regarding ENO’s 2021 Reliability Plan.

We are continuing to make progress on our 100% backbone and lateral inspection and repair program. Of the 13 feeders planned for 2021: 7 are completed, 4 are in construction, and 2 are not yet started. Following last year’s historic hurricane year in Louisiana, we front-loaded the year with our contract crews to complete as much work as possible prior to storm season beginning.

Our Fix-It-Now (“FIN”) reliability crew continues to work on performing infrared inspections of distribution facilities to identify and prevent outages that could result from imminent failure conditions as well as investigating repeat outages to assess and repair the fundamental cause of the outage. The crew completed work on more than 41 separate locations in the city during the reporting period.

We have completed our cyclical pole inspections for the year and restored or replaced all poles identified as deficient in those inspections. We continue our five-year plan to replace all non-restorable poles.

In the Distribution Automation Acceleration program, work has continued connecting existing reclosers to the growing communications network. Currently, approximately 41% of reclosers are on the automated network. We have also completed installation of three new reclosers with two more planned for later this year.

In the Underground program, while working in conjunction with planned transmission/substation work, we identified work to be performed on three sets of substation exit cables that could yield significant reliability benefits, reducing the potential for customer


interruptions. These are the points where power leaves the substation, and a fault could affect many customers. One of these projects is complete, one is under construction and the last is scheduled to be worked by the end of the year.

The Central Business District (CBD) Mesh Network Action Plan was developed mid-2021 and is underway. Of the 10 transformers planned to be replaced in 2021, six have been replaced and four are scheduled. We have sampled oil on 6 transformers and are evaluating options for fire protection to be installed.

Also attached hereto is a schedule of Transmission reliability projects scheduled to be worked in 2021, with costs incurred through September 2021.


ENO is available to discuss this report, and reliability in general, in further detail, if desired.

ENO 2021 Distribution Reliability Plan Project Progress

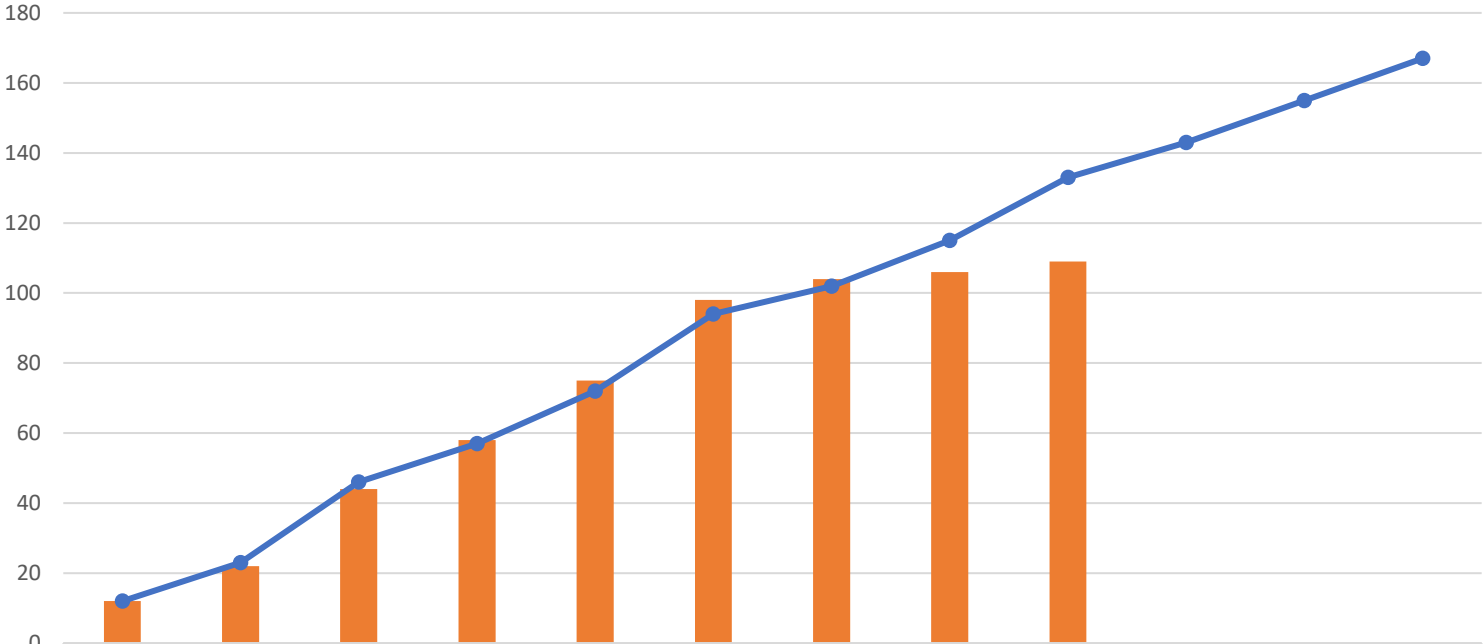

Actual Complete	Jan	Feb	Mar	Apr	May	June	July	Aug	Sept	Oct	Nov	Dec
Target Complete	12	23	46	57	72	94	102	115	133	143	155	167

ENO 2021 Distribution Plan Spend

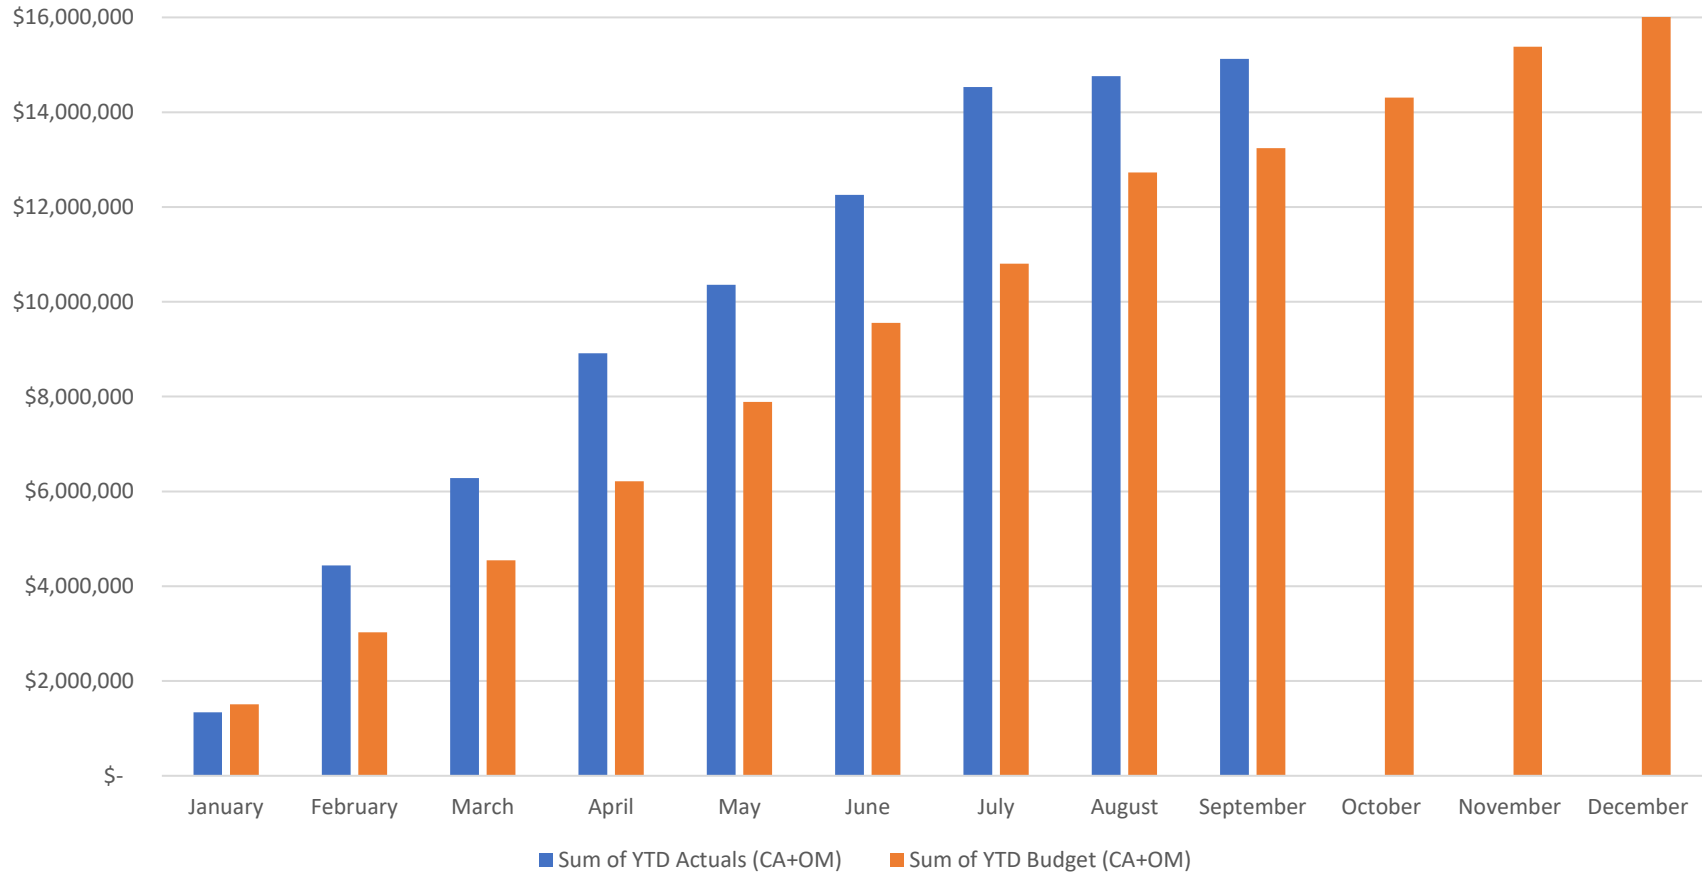

Funding Project	Sum of YTD Actuals	Sum of YTD Budget	Sum of YTD Variance
Internal (F1PPDA0198)	\$ 1,088,350	\$ 965,711	\$ 122,639
DA Acceleration / Sectionalization (F1PPDA1250)	\$ 40,047	\$ 368,909	\$ (328,862)
Focus (F1PPDA1750)	\$ (115,855)	\$ 386,523	\$ (502,378)
Outage Causal Analysis (F1PPDA2650)	\$ -	\$ 22,959	\$ (22,959)
100% Lateral, FIN & Other Strategic Reliability (F1PPU25021)	\$ 8,257,536	\$ 7,779,587	\$ 477,949
Equipment Inspection & Maintenance (F1PPDA0598)	\$ 35,867	\$ 37,692	\$ (1,825)
Backbone (F1PPDA0989)	\$ 537,795	\$ 195,213	\$ 342,582
Underground Safety, Network Improvement & Replacement (F1PPDA1550, F1PPU25008, F1PPUA5002)	\$ 778,991	\$ 1,472,924	\$ (693,933)
Pole Program (F1PPUA5001)	\$ 2,312,474	\$ 1,430,895	\$ 881,579
Grid Mod Make Ready Work (F1PPUMKRED)	\$ 7,401	\$ 72,675	\$ (65,274)
Conti Street Reconstruction (F1PPU27263)	\$ 2,185,935	\$ 1,405,402	\$ 780,533
Total	\$ 15,128,541	\$ 14,138,490	\$ 990,051

Note: We are ahead of our year-to-date target on spending due to front loading reliability work before storm season that did not align with the budget as originally projected. Our pole budget was overrun with additional spend in the Algiers area in conjunction with work done by Entergy Louisiana. We had a large accrual from end of 2020 reversed resulting in the negative spend in Focus.

2021 Transmission Reliability Project Status Updates

WO #s	Substation	Project Status	Work Description	Construction Start Date	EST ISD	Actual ISD	Estimated 2021 Project Cost	YTD Actuals at end of September 2021
C6PPGR0152	CURRAN	Complete	Upgrade SCADA RTU	2/1/2021	2/5/2021	2/23/2021	\$ 195,500	\$ 75,382
C6PPBU1529	NAPOLEON	Complete	Replace SEL-287 V with SEL-451 230kV Cap Bank Relay	1/18/2021	1/29/2021	3/8/2021	\$ 330,000	\$ 70,291
C6PPBU1553	NAPOLEON	Complete	Upgrade the D20 Supervisory Control Data Acquisition (SCADA) R	1/1/2021	1/31/2021	3/22/2021	\$ 207,500	\$ 103,737
C6PPBU1490	PAUGER	Complete	Replace the SCADA Remote Terminal Units (RTU) with an RTAC RT	11/30/2020	12/11/2020	4/19/2021	\$ 166,500	\$ 103,121
C6PPGR0153	SHERWOOD FOREST	Complete	Replace/upgrade SCADA RTU Type: D-20 ME (Non-Outage)	3/1/2021	3/5/2021	4/22/2021	\$ 126,000	\$ 39,565
C6PPGR0164	NOTRE DAME	Complete	Replace / Upgrade SCADA RTU Type: D-20	3/1/2021	3/31/2021	5/17/2021	\$ 143,000	\$ 46,198
C6PPGR0140	DERBIGNY	Complete	Replace 1513-2 Feeder Breaker	1/11/2021	1/22/2021	5/28/2021	\$ 292,000	\$ 154,954
C6PPGR0089	MARKET 230	Complete	Install Only - Replace 230kv OCB N2117	4/12/2021	5/21/2021	6/2/2021	\$ 383,000	\$ 207,422
C6PPGR0184	MARKET 230	Complete	Replace 230kv OCB N2111	5/21/2021	5/21/2021	6/2/2021	\$ 330,000	\$ 310,400
C6PPGR0227	MARKET 230	Complete	AT1 Life Extension	4/12/2021	5/21/2021	6/2/2021	\$ 489,500	\$ 725,609
C6PPBU1552	JOLIET	Complete	Replace / Upgrade SCADA RTU Type: D-20	6/7/2021	6/18/2021	7/27/2021	\$ 104,500	\$ 187,242
C6PPGR0142	DERBIGNY	In Progress	Replace OCB Main Breaker 15T2-6 and Disconnects	10/18/2021	11/12/2021		\$ 242,000	\$ 157,320
C6PPGR0158	DERBIGNY	In Progress	Replace 24kV OCB 1509-2	10/18/2021	11/12/2021		\$ 242,000	\$ 26,958
C6PPGR0217	SHERWOOD FOREST	In Progress	Replace Transformer T2	10/11/2021	11/19/2021		\$ 852,000	\$ 373,548
C6PPGR0183	MARKET 230	In Progress	Replace 230kv OCB N7209	11/8/2021	11/26/2021		\$ 330,000	\$ 145,780
C6PPBU1549	AVENUE C	In Progress	Replace T2 (with a 115-13.8kV 40MVA LTC)	9/1/2021	11/26/2021		\$ 825,000	\$ 158,007
C6PPGR0216	PONTCHARTRAIN PARK	In Progress	Replace SCADA RTU (Westronic)	11/12/2021	11/30/2021		\$ 104,500	\$ 48,044
C6PPGR0215	HOLIDAY	In Progress	Upgrade SCADA RTU (GE Energy Svcs)	12/10/2021	12/30/2021		\$ 104,500	\$ 28,011
C6PPCTMP15	NOTRE DAME	In Progress	Add 3 DGA Monitor	12/1/2021	12/31/2021		\$ 182,500	\$ 365,449
C6PPBU1571	PAUGER	Deferred	Add Two (2) DGA Monitors	3/1/2022	3/31/2022		\$ 138,000	\$ -
C6PPGR0143	LOWER COAST	Deferred	T2 (Life extension-add oil filtration, complete rebuild of LTC, repla	10/11/2022	11/19/2022		\$ 660,000	\$ 110,516
F1PPU51158	Gulf Outlet 115kV: Inst Cap Ba	Complete	Install new capbank	5/1/2020	12/1/2020	9/26/2020	\$ 45,874	\$ 83,137
F1PPUX4897	Tricou- Energize Xfmr T2	Complete	Install new Transformer	2/15/2020	12/31/2020	11/23/2020	\$ 316,359	\$ 296,854
F1PPU75782	Upgrade Ave C - Paris Tap line	In Progress	Upgrade TLine and switches and bus work at Ave. C.	TBD	6/1/2022	TBD	\$ 553,782	\$ 163,735
F1PPU51353	Lower Coast 230kV- Add Breaker	In Construction	Install high side breakers	TBD	6/1/2022	TBD	\$ 4,664,394	\$ 3,121,589
F1PPU51248	Curran 230kV- Add Breaker	In Construction	Install high side breakers	TBD	6/1/2023	TBD	\$ 2,520,777	\$ 1,901,337

CERTIFICATE OF SERVICE

Docket No. UD-17-04

I hereby certify that I have served the required number of copies of the foregoing report upon all other known parties of this proceeding, by the following: electronic mail, facsimile, overnight mail, hand delivery, and/or United States Postal Service, postage prepaid.

Ms. Lora W. Johnson, CMC, LMMC
Clerk of Council
Council of the City of New Orleans
City Hall, Room 1E09
1300 Perdido Street
New Orleans, LA 70112

Erin Spears, Chief of Staff
Bobbie Mason
Council Utilities Regulatory Office
City of New Orleans
City Hall, Room 6E07
1300 Perdido Street
New Orleans, LA 70112

David Gavlinski
Council Chief of Staff
New Orleans City Council
City Hall, Room 1E06
1300 Perdido Street
New Orleans, LA 70112

Sunni LeBeouf
City Attorney Office
City Hall, Room 5th Floor
1300 Perdido Street
New Orleans, LA 70112

Norman White
Department of Finance
City Hall, Room 3E06
1300 Perdido Street
New Orleans, LA 70112

Hon. Jeffery S. Gulin
3203 Bridle Ridge Lane
Lutherville, MD 21093

Andrew Tuozzolo
CM Moreno Chief of Staff
1300 Perdido Street, Room 2W40
New Orleans, LA 70112

Jonathan M. Rhodes
Director of Utilities, Mayor's Office
City Hall, Room 2E04
1300 Perdido Street
New Orleans, LA 70112

Clinton A. Vince
Presley R. Reed, Jr.
Emma F. Hand
Herminia Gomez
Dee McGill
Dentons US LLP
1900 K Street, NW
Washington, DC 20006

Basile J. Uddo
J.A. "Jay" Beatmann, Jr.
c/o Dentons US LLP
The Poydras Center
650 Poydras Street, Suite 2850
New Orleans, LA 70130-6132

Joseph W. Rogers
Victor Prep
Byron S. Watson
Cortney Crouch
Legend Consulting Group
6041 South Syracuse Way, Suite 105
Greenwood Village, CO 80111

Courtney R. Nicholson
Vice President, Regulatory Affairs
Entergy New Orleans, LLC
1600 Perdido Street
Mail Unit L-MAG-505B
New Orleans, LA 70112

Brian L. Guillot
Leslie LaCoste
Entergy Services, LLC
639 Loyola Avenue
Mail Unit L-ENT-26E
New Orleans, LA 70113

Emily K. Leitzinger
Mid-City Neighborhood Organization
4313 Palmyra Street
New Orleans, LA 70119

Julianna D. Padgett
Carrollton Riverbend Neighborhood Assn.
935 Dante Street
New Orleans, LA 70118

Jacob Rickoll
Tulane Canal Neighborhood Association
2301 Conti Street
New Orleans, LA 70119

Keith Hardie
Maple Area Residents, Inc.
618 Audubon Street
New Orleans, LA 70118

Errol Smith
Bruno and Tervalon
4298 Elysian Fields Avenue
New Orleans, LA 70122

Derek Mills
Seth Cureington
Kevin T. Boleware
Entergy New Orleans, LLC
1600 Perdido Street
Mail Unit L-MAG-505B
New Orleans, LA 70112

Joseph J. Romano, III
Tim Rapier
Therese Perrault
Entergy Services, LLC
639 Loyola Avenue
Mail Unit L-ENT-4C
New Orleans, LA 70113

Logan Atkinson Burke
Sophie Zaken
Alliance for Affordable Energy
4505 S. Claiborne Avenue
New Orleans, LA 70125

Ian Dreyer
Parkview Neighborhood Association
432 N. Anthony Street, Suite 303
New Orleans, LA 70119

Abigail Sebton
Urban Conservancy Petition
1307 OC Haley Boulevard #307
New Orleans, LA 70113

Monique Harden
Deep South Center for
Environmental Justice, Inc.
3157 Gentilly Boulevard, #145
New Orleans, LA 70122

Renate Heurich
350 Louisiana-New Orleans
1407 Napoleon Avenue, #B
New Orleans, LA 70115

Ed Morris
Yolanda Y. Grinstead
Sewerage and Water Board
625 St. Joseph Street, Room 201
New Orleans, LA 70165

Luke F. Piontek
Judith Sulzer
Roedel, Parsons, Koch, Blache, Balhoff
& McCollister
8440 Jefferson Highway
Suite 301
Baton Rouge, LA 70809

Eric J. Songy
Algiers Neighborhood Presidents Council
P.O. Box 740446
New Orleans, LA 70174

Warrenetta C. Banks
Lower 9 Resilient
5130 Chartres Street
New Orleans, LA 70117-3808

Arthur J. Johnson
Lower 9th Ward Center for Sustainable
Engagement and Development
5227 Chartres Street
New Orleans, LA 70117

David Dalia
609 Dumaine Street
New Orleans, LA 70115-3210

Dawn Hebert
6846 Lake Willow Dr.
New Orleans, LA. 70126

Denise T. Turbinton
931 Mazant St.
New Orleans, LA 70117

New Orleans, Louisiana, this 15th day of December 2021.



Courtney R. Nicholson
